

PMO and Project Delivery Transformation with Microsoft Project Online



PMO
Conference
London
2018

P PROGRAM
FRAMEWORK

Gero Renker
Director



Chris Ward
Head of PMO

Introducing Program Framework

Microsoft Cloud for PPM

Solution Strategy

Integration

Implementation

Custom Solutions

Adoption Services

Managed Services



Gold Project and Portfolio Management
Silver Collaboration and Content
Silver Small and Midmarket Cloud Solutions



2017 Partner of the Year Winner
Cloud Productivity Award

Microsoft Partner of the Year
2016 Finalist
Project and Portfolio Management




Talking Points

Introducing Microsoft Cloud for PPM

Nottingham Trent University story

Relevance for your own PMO

Microsoft Cloud – Office 365



Enterprise:
PPM



Team:
Organise & Collaborate



Individual:
Manage Tasks



Calendar



Power BI



Delve



PowerApps



Dynamics 365



PowerPoint



Excel



Project



Teams



Flow



Security & Compliance



To-Do



Forms



SharePoint



Video



OneDrive



Social Engagement



Visio



OneNote



StaffHub



Word



Outlook



Store



Yammer



Partner



Stream



People



Sway



Planner




Tasks

Project Online



Program Management



Demand Management




Portfolio Analytics & Selection




Business Intelligence & Reporting




Team Collaboration & Social



Issues & Risk Management



Schedule Management



Time Reporting



Resource Management



Financial Management

Introducing Nottingham Trent University



30,000 Students 4,000 Staff



3 Campus's in Nottingham

- City Centre
- Clifton
- Brackenhurst (near Southwell)

> £350m investment

37k applications worldwide (UCAS 2016)

93% of students would recommend studying at NTU

World-Leading Research

96% of our graduates are employed or engaged in further study six months after leaving

The Problem in January 2016....

No authority/decision making body

Inconsistent use of the NTU Project Framework

Portfolio Reporting was a cottage industry


No coherent approach to Resource Management

No single version of the truth


No Quality Assurance

In danger of not being relevant!


NTU's Journey

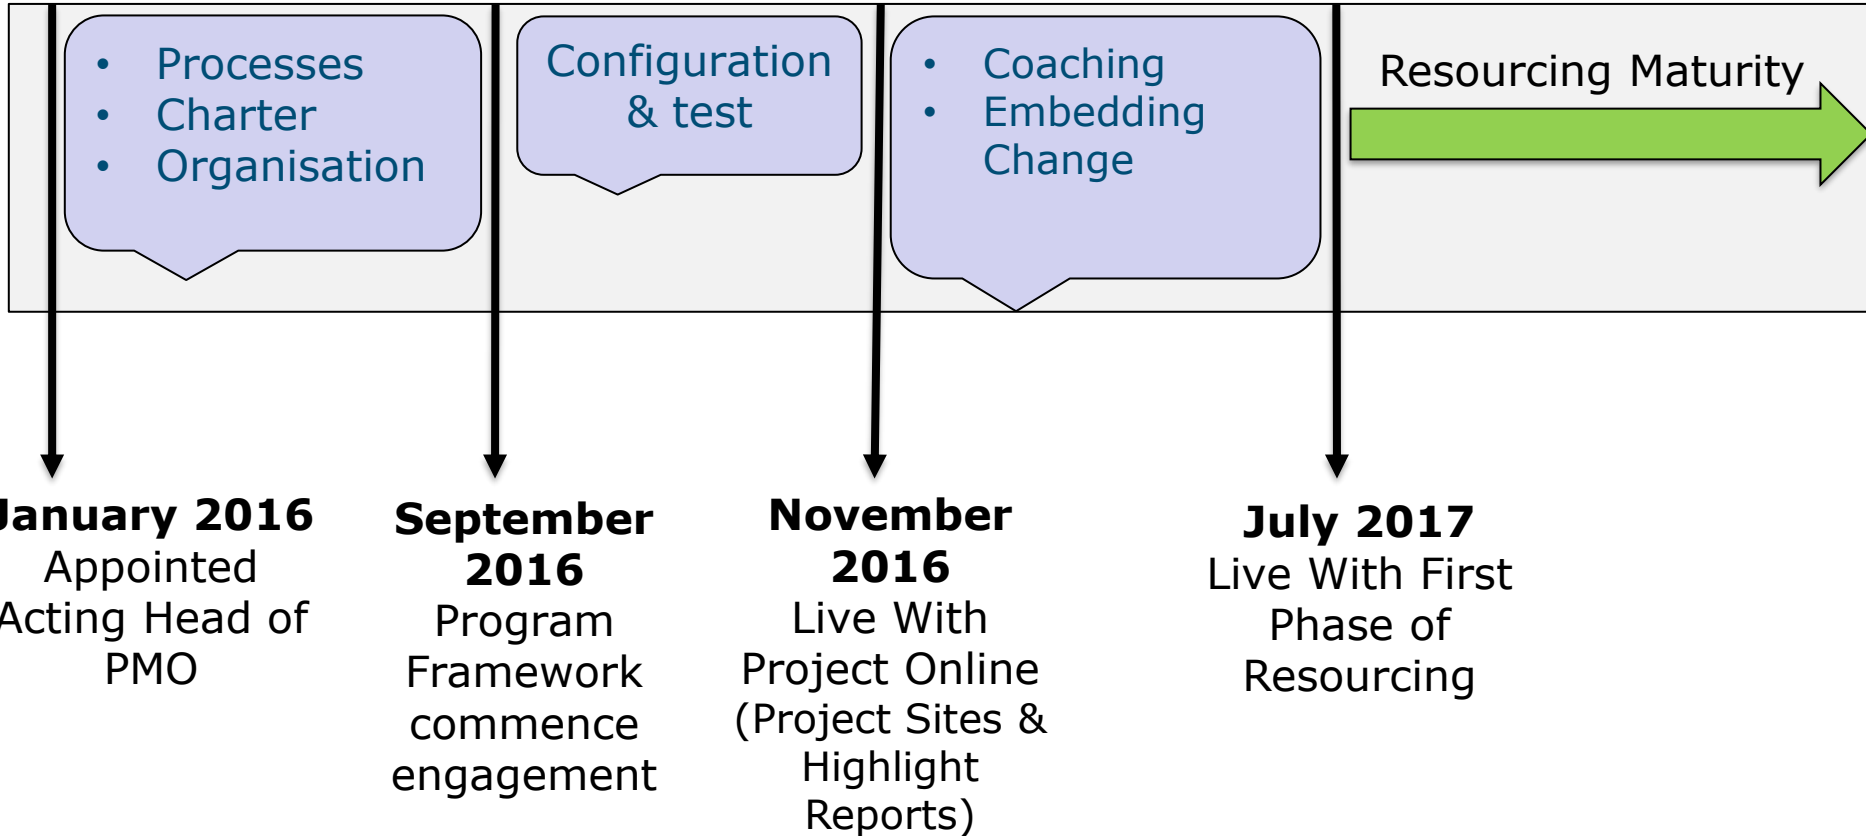

Sample Highlight Report

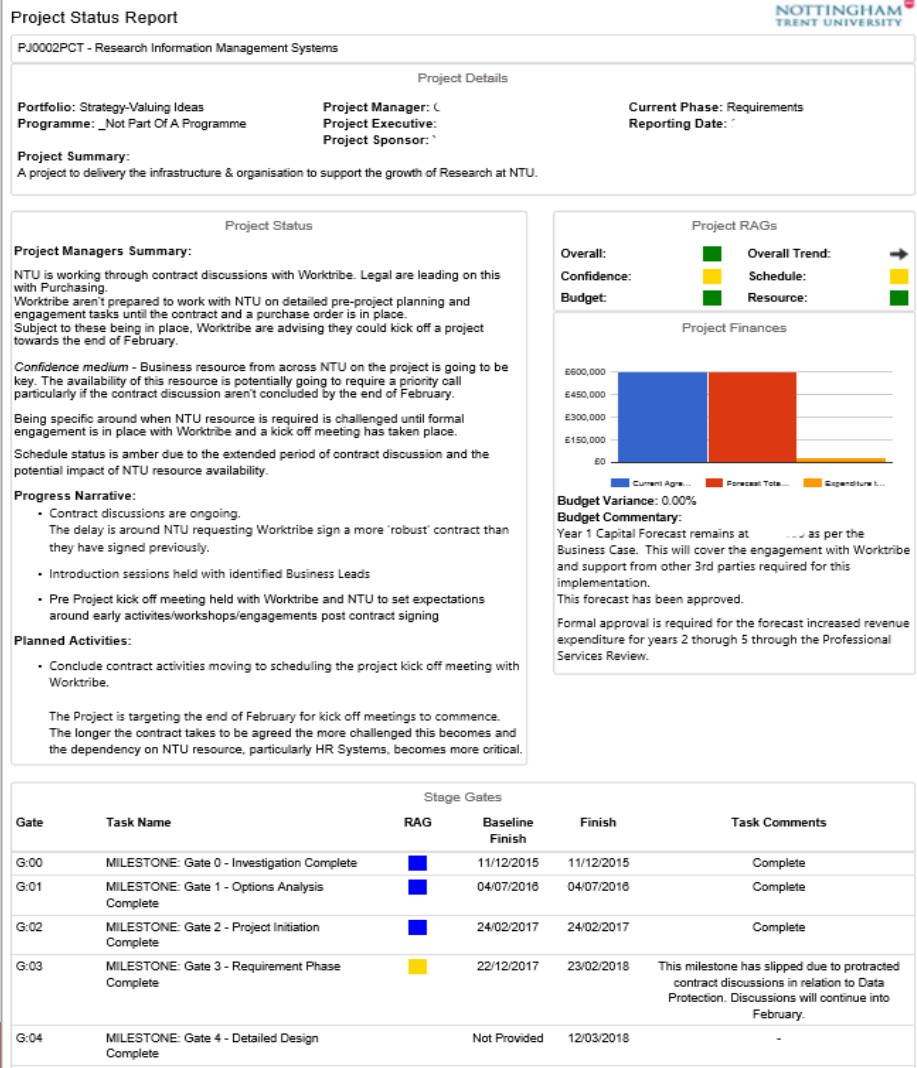

Sample Resource Center

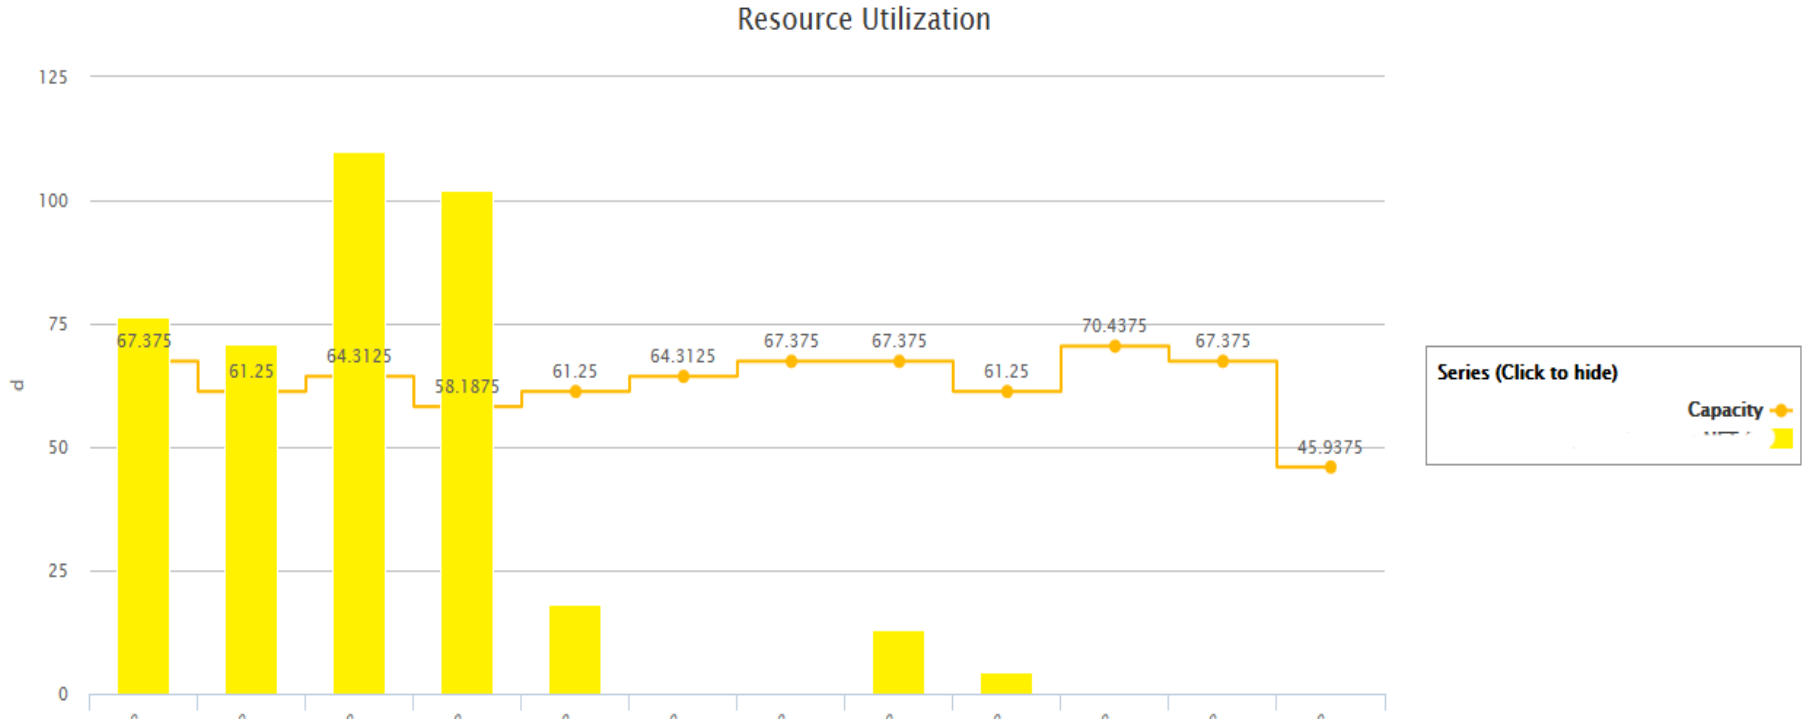


Sample Dashboard

Project Data_PMO
PROJECT OVERVIEW


Overview of Current Open Projects

Breakdown of Project Resource




Project Name	Project Actual Start Date	Current Phase Completes
Acar	02 May 2016	Apr 4, '18
A	03 July 2017	Feb 20, '18
Al...	12 October 2017	Feb 28, '18
Al...	04 January 2016	Jan 8, '18
Al...	01 September 2017	Jan 19, '18
Al...	24 May 2017	Feb 8, '18
Al...	01 September 2016	May 17, '18
Al...	16 October 2017	Jan 31, '18
Al...	24 October 2017	Feb 23, '18
Al...	01 April 2016	Jan 31, '18
Al...	10 August 2015	May 4, '18
Al...	06 March 2017	Nov 30, '18
Al...	02 May 2017	Mar 14, '18
Al...	08 January 2018	Feb 16, '18
Al...	02 December 2016	Feb 28, '18
Al...	17 January 2017	Jan 18, '19
Al...	03 August 2015	03 Aug '15
Al...	12 October 2016	Jan 31, '18
Al...	07 December 2015	Feb 23, '18
Al...	03 January 2018	03 Jan '18
Al...	11 August 2016	Feb 13, '18
Al...	02 November 2016	Jun 6, '19
Al...	13 February 2017	Feb 27, '18
Al...	30 October 2017	Jan 31, '18
Al...	18 September 2017	Jan 31, '18


Forecasted Year of Project Closure



Projects by Current Phase

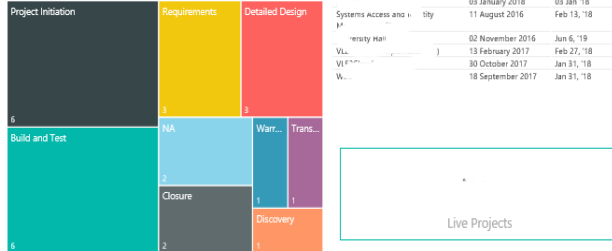

Number of Active Risks per Project

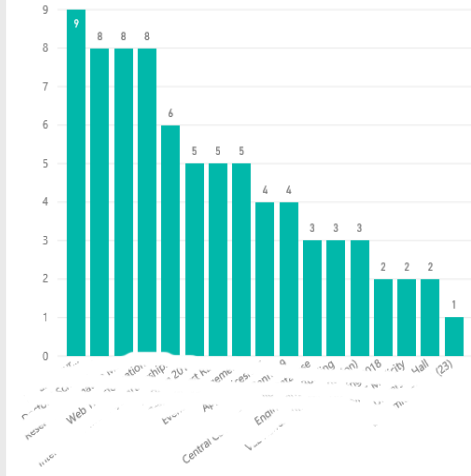

Number of Active Issues per Project



Project Data_PMO
EXCEPTION REPORTING

10cf-4c19-aa08-db98776c1e36/contentlist

The Benefits

Projects are now delivered within a Framework which has enabled a 'single version of the truth'

We have simplified our reporting at Project, Programme & Portfolio levels

We have strong Quality Assurance in place across the PMO

The approach we are taking around Resource Management is now facilitating a robust conversation with regards to Project Resourcing

We have a Portfolio Backlog reflecting the Strategy, supporting delivery forecasts & re-prioritisation

The PMO is relevant! **But we are not being complacent...**

Some Take-Aways

The decision on an implementation partner is as key as the solution decision

Agree & establish your project lifecycle before you implement the solution

Consider the impact on the project community so you can bring them on the journey

Treat the implementation as a Project

PowerBI working with Project Online creates a strong user experience for Senior Stakeholders

Be realistic with your objectives & approach to implementation


Strategies for Rapid Success



Office 365 Platform Readiness

- Tenant is ready
- Focus on key objectives
- Users are already enrolled
- Single sign on
- QuickStart
- Start with basic 20 configuration
- Common I
- Config
- Platform
- Report
- Common I
- Process
- ...all out of the box

Power BI Benefit

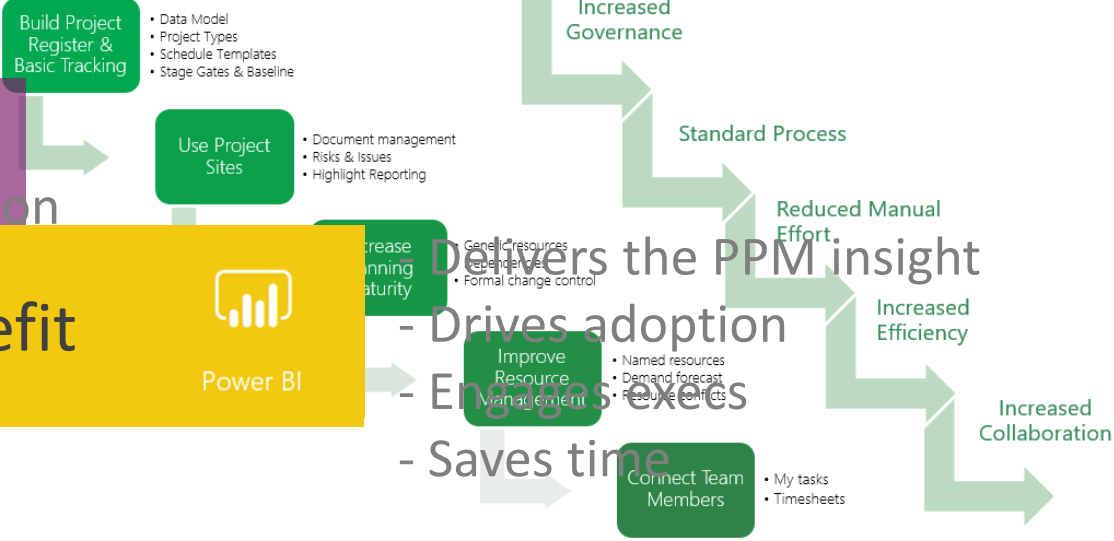

Next Steps

Read this and other case studies: programframework.com/case-studies



Next Steps

Attend our Seminar: programframework.com/events



Thu 05 Jul | Program Framework London...

Rapidly Transform your PMO with Microsoft Cloud

Join this 2-hour morning session in the City
to find out how your PMO can transform
itself in a very short time with the help of
Microsoft Cloud

[Register Now](#)

Next Steps

See us in the exhibition hall and find out more about...



Project



SharePoint



Power BI



Teams



Planner



Next Steps



TRIAL

Assisted trials for Project Online or Office365 with free licensing



DEMO for your Team

Full solution demo personalized for your context and background



PROTOTYPE

Building your prototype environment in a week!

gero.renker@programframework.com

0771 4720007
